

# MONTHLY PROJECT REPORT

## SR 16 Tacoma Narrows Bridge Project

JANUARY 2003

**Project Location:** SR 16, Jackson Avenue to 36<sup>th</sup> Street


**PIN:** 301699A

**WIN:** C01699C, C01699D

**Contractors:** Tacoma Narrows Constructors, A Joint Venture (Design/Build); TransCore, L.P (Toll System Supply and Installation )

<b>Project Cost Summary:</b>	<b>\$Millions</b>	<b>Expended</b>
Design/Build Contract	615.0	96.2
Toll System Contract	9.2	0.3
WSDOT Oversight	41.0	1.7
Contingencies	54.7	0.7
Phase I Dev. Cost (UIW)	40.5	39.9
Total	760.4	138.8
Total Expended/Total Cost	18.3%	

**Project Cash Flow:** (01-03 Biennium in Millions)

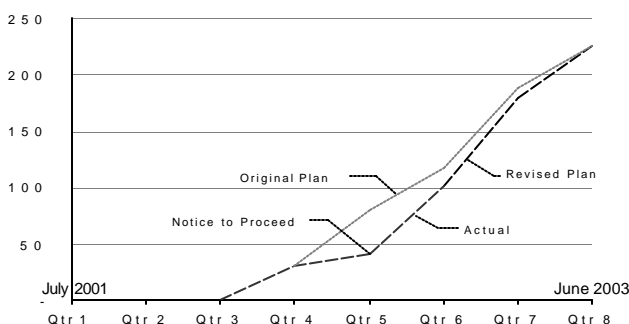


### Project Schedule Status:

- No schedule variance
- No delay on the Critical Path
- Contract Milestones are scheduled ahead of Contract dates


### Contract Milestones Overview:

Milestone	Contract	TNC	Months Ahead
Provide Final Plans and Spec. for Toll Facilities	25Sep03	16May03	4.4
Place order for Saddles	17Feb04	18Jul03	7.1
Complete new bridge substructure	12May05	11Apr05	1.0
Guaranteed TCAAS Installation Readiness Date	08Dec05	19Sep05	2.7
Lift first deck unit	07May06	14Feb06	2.7
Complete Superstructure joining of deck sections	03Dec06	29Aug06	3.2
Guaranteed Tolling Completion Date	02Apr07	02Apr07	0.0
Guaranteed Project Substantial Completion Date	26Feb08	26Feb08	0.0

### Project Summary Schedule:

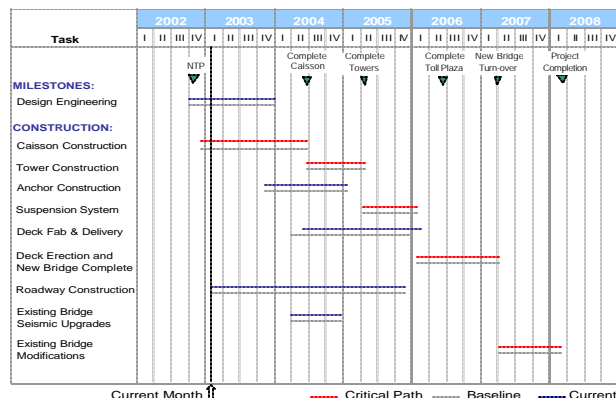

### Project Progress To Date: (% Complete)



1. Weighted 7% Design progress and 93% Construction progress

### Progress Highlights for month of January 2003:

- Permanent construction started at 24<sup>th</sup> Street, TNC takes over segment
- Anchor Line materials ordered
- Completed design and shop drawings for Caisson Cutting Edge, fabrication continues



Portion of Caisson Cutting Edge

### Quality Control:

- Developing Audit Process
- Developing key indicators & performance measures

### Risks/Challenges/Issues:

- Acquisition of additional Right of Way Westside of the bridge
- Supplemental Noise Study at 36<sup>th</sup> Street

### Upcoming Activities for February:

- Project Partnering Sessions
- Soil Remediation at Living War Memorial Park
- Median work on SR16 at 24<sup>th</sup> Street

### Public Information:

- Project Open House held on January 30<sup>th</sup> at Gig Harbor
- Daily nighttime construction updates and noise feedback form included on the website
- 24-Hour phone line for nighttime construction updated daily (253) 620-4440

For More Information, Call us toll free at 1.877.762.7769

Or Visit our Website: [www.wsdot.wa.gov/projects/sr16narrowsbridge/](http://www.wsdot.wa.gov/projects/sr16narrowsbridge/)

